

QuickPay Delay Rate – All Defense Projects

2024-02-02

1 QuickPay Expanded Sample

- Consider ALL defense projects that started b/w FY 2010 and FY 2012
- Only consider delays not caused by action types “D”, “A”, “L”, “G”
- Restrict to June 30, 2012 – QP expanded to all projects after that

Table 1: Full sample of Fixed Price Contracts

Dependent Variable: Model:	(1)	(2)	Percentage delay rate			
			(3)	(4)	(5)	(6)
<i>Variables</i>						
Constant	12.52*** (0.15)	20.44*** (0.34)				
Treat	1.37*** (0.21)	-0.63*** (0.20)	-0.70*** (0.20)	-1.34*** (0.22)	-1.41*** (0.22)	-1.84*** (0.23)
Post	3.61*** (0.21)	1.30*** (0.48)				
Treat × Post	1.37*** (0.30)	1.65*** (0.27)	1.41*** (0.27)	1.32*** (0.27)	1.26*** (0.27)	1.33*** (0.27)
Controls	No	Yes	Yes	Yes	Yes	Yes
<i>Fixed-effects</i>						
Year-Quarter			Yes	Yes	Yes	Yes
Task				Yes	Yes	Yes
Sub-agency					Yes	Yes
NAICS						Yes
<i>Fit statistics</i>						
Observations	310,485	310,350	310,350	310,350	310,350	309,417
R ²	0.00323	0.17193	0.18320	0.20006	0.20158	0.20789
Within R ²			0.16562	0.15463	0.15472	0.15201

Clustered (Project ID) standard-errors in parentheses

*Signif. Codes: ***: 0.01, **: 0.05, *: 0.1*

Controls include initial budget, offers, duration, their interaction with post, and project stage.

Table 2: Full sample of Cost Plus Contracts

Dependent Variable:	Percentage delay rate					
Model:	(1)	(2)	(3)	(4)	(5)	(6)
<i>Variables</i>						
Constant	8.92*** (0.24)	24.20*** (1.15)				
Treat	-2.02*** (0.43)	1.31*** (0.41)	1.31*** (0.41)	0.31 (0.43)	0.39 (0.44)	0.13 (0.45)
Post	2.98*** (0.33)	-2.05 (1.58)				
Treat $\times$ Post	0.68 (0.58)	0.28 (0.55)	0.18 (0.55)	0.62 (0.56)	0.58 (0.56)	0.60 (0.56)
Controls	No	Yes	Yes	Yes	Yes	Yes
<i>Fixed-effects</i>						
Year-Quarter			Yes	Yes	Yes	Yes
Task				Yes	Yes	Yes
Sub-agency					Yes	Yes
NAICS						Yes
<i>Fit statistics</i>						
Observations	47,879	47,831	47,831	47,831	47,831	47,831
R ²	0.00318	0.18007	0.18308	0.19974	0.20028	0.20403
Within R ²			0.17552	0.16954	0.16961	0.16890

Clustered (Project ID) standard-errors in parentheses

*Signif. Codes: ***: 0.01, **: 0.05, *: 0.1*

Controls include initial budget, offers, duration, their interaction with post, and project stage.

Table 3: JOBS act – Sample of Fixed Price Contracts

Dependent Variable:	Percentage delay rate				
Model:	(1)	(2)	(3)	(4)	(5)
<i>Variables</i>					
Constant	9.46*** (0.22)	20.47*** (0.34)			
Treat	1.77*** (0.32)	-1.76*** (0.27)	-0.22 (0.30)	-0.80** (0.32)	-1.32*** (0.33)
Post	1.67*** (0.25)	1.31*** (0.48)			
JOBS act	5.00*** (0.29)				
Treat $\times$ JOBS act	-0.83* (0.42)	1.76*** (0.28)	-0.77** (0.39)	-0.86** (0.39)	-0.82** (0.39)
Treat $\times$ Post	1.79*** (0.35)	1.01*** (0.29)	1.70*** (0.31)	1.63*** (0.31)	1.66*** (0.32)
Controls	No	Yes	Yes	Yes	Yes
<i>Fixed-effects</i>					
Year-Quarter			Yes	Yes	Yes
Task				Yes	Yes
NAICS					Yes
<i>Fit statistics</i>					
Observations	310,485	310,350	310,350	310,350	309,417
R ²	0.00451	0.17203	0.18321	0.20007	0.20669
Within R ²			0.16563	0.15465	0.15232

Clustered (Project ID) standard-errors in parentheses

*Signif. Codes: ***: 0.01, **: 0.05, *: 0.1*

Controls include initial budget, offers, duration, their interaction with post, and project stage.

Table 4: No Set Aside Used – Sample of Fixed Price Contracts

Dependent Variable: Model:	(1)	Percentage delay rate			
		(2)	(3)	(4)	(5)
<i>Variables</i>					
Constant	12.53*** (0.15)	21.07*** (0.41)			
Treat	3.31*** (0.28)	-0.37 (0.27)	-0.47* (0.27)	-1.29*** (0.30)	-1.77*** (0.31)
Post	3.57*** (0.21)	1.18** (0.57)			
Treat $\times$ Post	0.84** (0.39)	1.43*** (0.36)	1.23*** (0.36)	1.20*** (0.36)	1.24*** (0.36)
Controls	No	Yes	Yes	Yes	Yes
<i>Fixed-effects</i>					
Year-Quarter			Yes	Yes	Yes
Task				Yes	Yes
NAICS					Yes
<i>Fit statistics</i>					
Observations	222,170	222,071	222,071	222,071	221,138
R ²	0.00367	0.17372	0.18371	0.20380	0.21214
Within R ²			0.16847	0.15769	0.15475

Clustered (Project ID) standard-errors in parentheses

*Signif. Codes: ***: 0.01, **: 0.05, *: 0.1*

Controls include initial budget, offers, duration, their interaction with post, and project stage.

Table 5: No C8A Participant – Sample of Fixed Price Contracts

Dependent Variable: Model:	(1)	Percentage delay rate			
		(2)	(3)	(4)	(5)
<i>Variables</i>					
Constant	12.52*** (0.15)	20.34*** (0.35)			
Treat	1.35*** (0.22)	-0.70*** (0.21)	-0.75*** (0.21)	-1.50*** (0.23)	-1.96*** (0.24)
Post	3.61*** (0.21)	1.39*** (0.49)			
Treat $\times$ Post	1.40*** (0.30)	1.77*** (0.28)	1.51*** (0.28)	1.42*** (0.28)	1.48*** (0.28)
Controls	No	Yes	Yes	Yes	Yes
<i>Fixed-effects</i>					
Year-Quarter			Yes	Yes	Yes
Task				Yes	Yes
NAICS					Yes
<i>Fit statistics</i>					
Observations	299,148	299,015	299,015	299,015	298,082
R ²	0.00322	0.17193	0.18344	0.20092	0.20771
Within R ²			0.16577	0.15479	0.15228

Clustered (Project ID) standard-errors in parentheses

*Signif. Codes: ***: 0.01, **: 0.05, *: 0.1*

Controls include initial budget, offers, duration, their interaction with post, and project stage.

Table 6: Projects that started before QP – Sample of Fixed Price Contracts


Dependent Variable: Model:	(1)	Percentage delay rate			
	(2)	(3)	(4)	(5)	
<i>Variables</i>					
Constant	12.52*** (0.15)	21.54*** (0.34)			
Treat	1.36*** (0.21)	-0.68*** (0.20)	-0.76*** (0.20)	-1.29*** (0.22)	-1.82*** (0.23)
Post	2.17*** (0.22)	-11.19*** (0.62)			
Treat × Post	-0.10 (0.32)	1.53*** (0.30)	1.30*** (0.30)	1.06*** (0.30)	1.13*** (0.30)
Controls	No	Yes	Yes	Yes	Yes
<i>Fixed-effects</i>					
Year-Quarter			Yes	Yes	Yes
Task				Yes	Yes
NAICS					Yes
<i>Fit statistics</i>					
Observations	242,359	242,276	242,276	242,276	241,352
R ²	0.00091	0.15414	0.16252	0.18144	0.18932
Within R ²			0.14837	0.13732	0.13520

Clustered (Project ID) standard-errors in parentheses

Signif. Codes: ***: 0.01, **: 0.05, *: 0.1

Controls include initial budget, offers, duration, their interaction with post, and project stage.

Fixed Price Contracts -- All NAICS codes

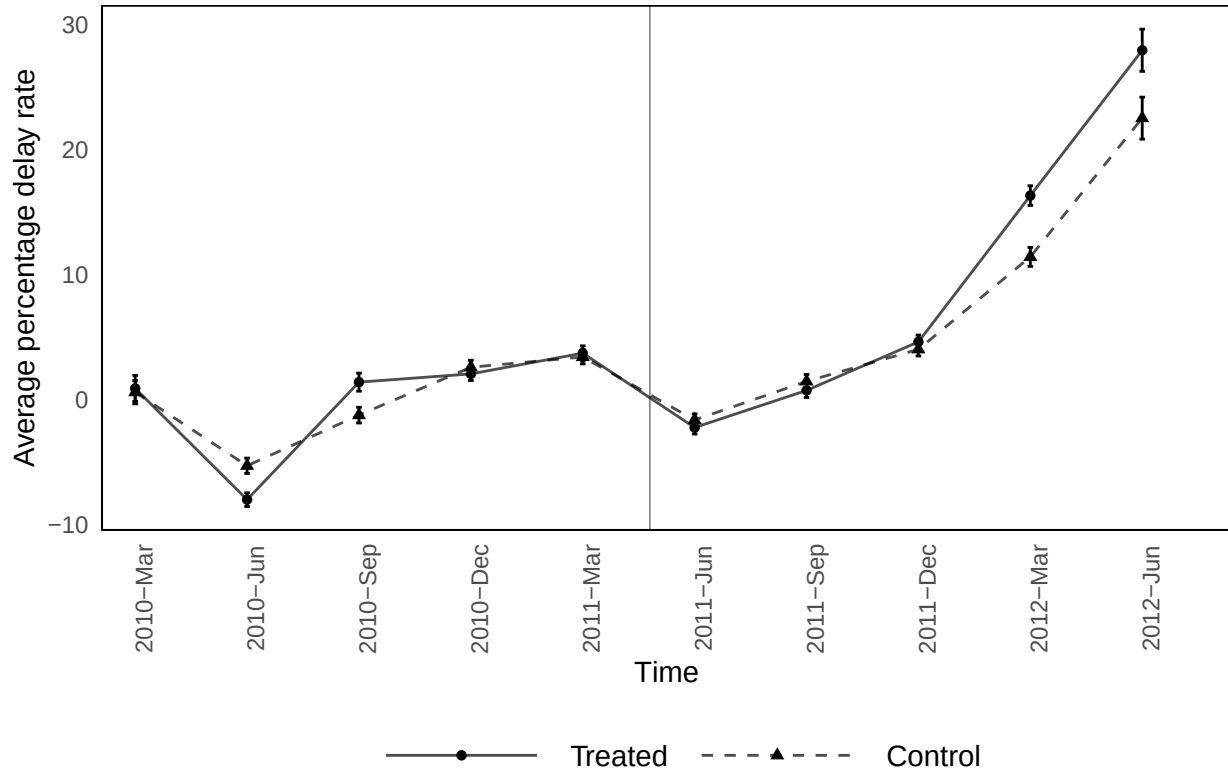

Fixed Price Contracts -- Top 20 NAICS codes in Barrot and Nanda

